
GreenCircle Certified Database Project

Project Status and Timeline Updates



Project Timeline Updates

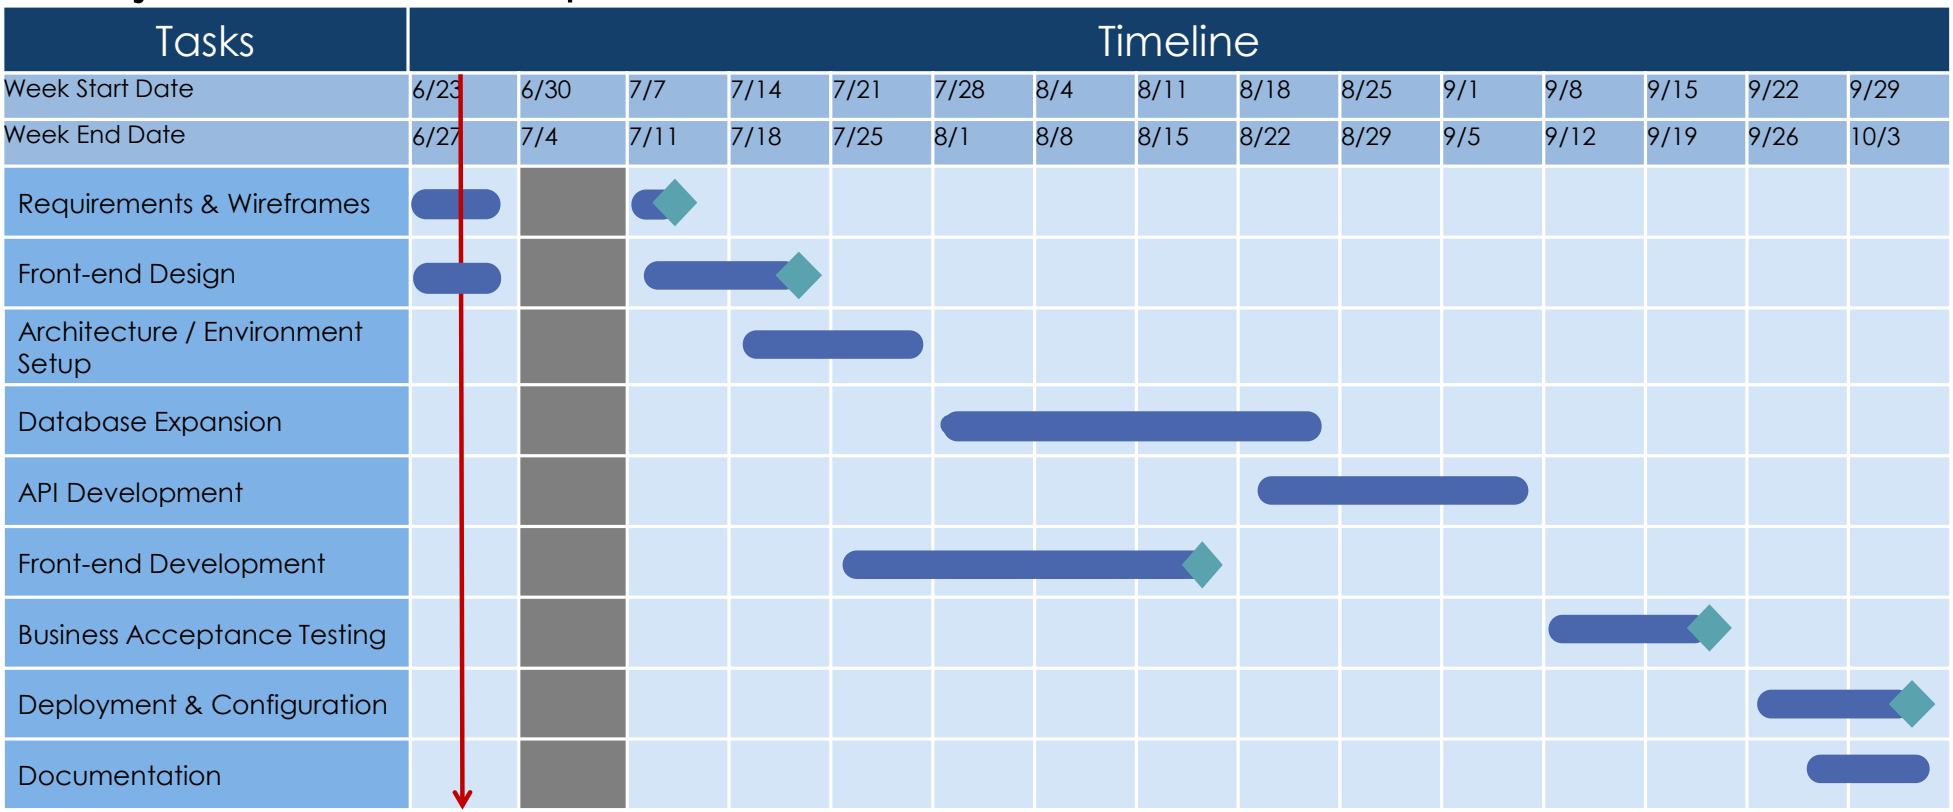

Milestones:
6/27 – Wireframes & Requirement complete
9/5 – Development Complete
9/19 – Testing Complete
10/3 – Go live

Coordination:
9/8 – 9/19 : Business Acceptance Testing, Defect Resolution
9/8 – 9/19 : API Testing with Amazon
9/22 – 10/3 : Deployment Activities


Scope Creep Analysis & Timeline Impact

Metric	Original	Revised	Increase
Timeline	14–18 weeks	34–40 weeks	+20–22 weeks

Area	Description
Client Requirements	User stories and requirements evolved during design.
Front-End Redesign	Expanded from basic UI to extensive front-end design
Product Management	Introduced multi-ID types (ASIN, UPC, GTIN, EAN) and import features.
Field Management	Included inline editing and dynamic field creation.
Dashboards	Added 10+ metrics, tracking, and role-based views.
Stakeholder Feedback	Multiple rounds of design revisions required.

- I had a family emergency that reduced my commitment to the project for a few weeks.
- The increased scope from the initial proposal with the additional enhancements has impacted the original timeline.
- The timeline reflects an accurate schedule to ensure quality and fits to the business needs of the system.

GreenCircle Certified Database Site Map

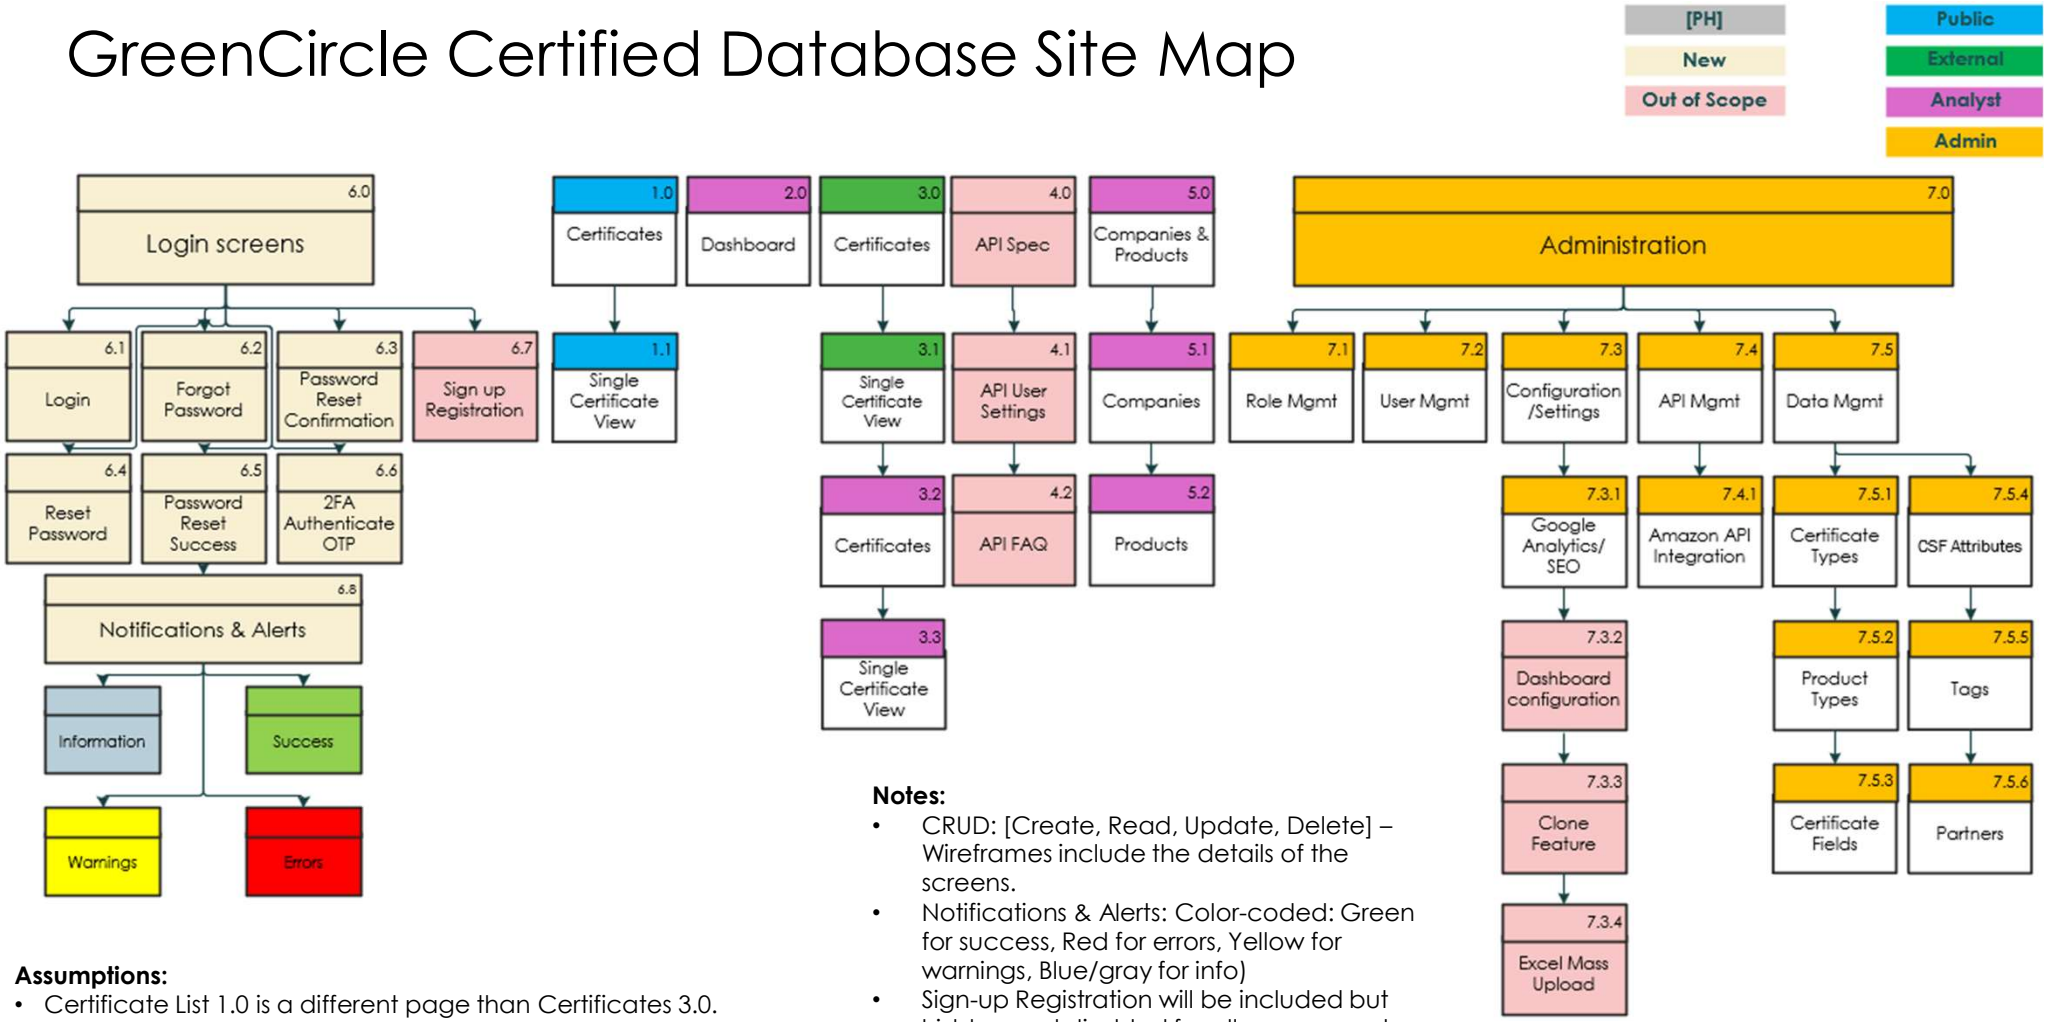

Assumptions:

- Certificate List 1.0 is a different page than Certificates 3.0.
- Admin will have the ability to Add, Edit or Delete a Certificate, Company, Products, Users, Certificate Type, Product Types and Tags.

Notes:

- CRUD: [Create, Read, Update, Delete] – Wireframes include the details of the screens.
- Notifications & Alerts: Color-coded: Green for success, Red for errors, Yellow for warnings, Blue/gray for info)
- Sign-up Registration will be included but hidden and disabled for all users except the admin.

Out of Scope Items – Initial Design Phase

- The following items are not included in the current scope and will be considered for future phases:
  - New Feature Requests Post-Freeze : Any new functionality or UX suggestions will be reviewed separately post-launch
  - Non-Core Page Redesigns: Pages not directly tied to core certificate workflows (e.g., user management, admin dashboards) are not part of the initial design scope.
  - Advanced Reporting & Analytics Modules: Custom reporting or dashboards requiring dynamic visualizations will be addressed in a future release.
  - Undocumented Features – Anything not captured in this document or related requirement files is excluded.
  - Integration Beyond Amazon Export: Any third-party system integration beyond current export scope will be handled as a separate project.
  - Clone Functionality – Selective field cloning for certificate records is not included.
  - Notifications & Alerts – Real-time user notifications are not part of this phase.
  - Undocumented Features – Anything not captured in this document or related requirement files is excluded

Note: Any additional functionality or enhancements outside this scope will follow the formal change request process and may be included in a post-launch roadmap.

October 3rd Go-live

- The adjusted timeline provides:
  - Adequate time for comprehensive development of expanded features
  - Proper testing cycles for the enhanced functionality
  - Quality assurance for the more complex integrations
  - Stakeholder alignment on enhanced deliverables

- Scope Evolution Highlights:
  - Enhanced Security Features - MFA, audit logging, role-based permissions
  - Advanced User Experience - Infinite scrolling, improved filtering, mobile considerations
  - Complex Data Management - Sophisticated product ID handling, multi-partner associations
  - Extended User Types - External partners, varied client access models

Design Revision Impact on Delivery

- Multiple UI design paths were explored throughout the project
- Functionality appeared inconsistently across versions (e.g., filters/buttons in some screens but missing in others)
- Comments and revisions introduced fragmentation and slowed alignment
- Final design direction is now established, but required more time than originally scoped
- Incremental requirements were introduced with additional scope delivered in fragments.
- As new features were added mid-cycle, screens often showed inconsistent functionality.
- Each revision improved the system but fragmented design artifacts and slowed decisions.
- We are now consolidating all approved elements into a single UI reference to avoid rework.
- This will improve quality, reduce QA cycles, and streamline final delivery.

Final Design Consolidation - Scope Locked

- Scope Freeze: No new functionality will be added. Existing design elements are being unified into one master reference.
- Fragmented Pages: Screens created during iterative revisions are being merged to ensure every approved feature appears consistently.
- Quality Focus: Consolidation eliminates hidden gaps, reduces rework, and accelerates the build and QA phases.
- Post-Launch Enhancements: Any new ideas identified after consolidation will be scheduled for a future release cycle.

Managing Scope and Change Control Plan

- Purpose: Structure future requests to maintain control over budget and timelines.
- Baseline Locked: the consolidated design is the development baseline.
- Transparency: All new requests will be assessed and estimated before inclusion.
- No Hidden Drift: Unapproved additions will be deferred to a future release phase.
- Process includes request intake, impact review, client approval, and timeline update.

Future changes will follow a simple estimate-and-approve process.

- Any additions will be reviewed for:
  - Timeline impact
  - Cost implication
  - System stability
- This ensures transparency and avoids unintentional delays during final phases.
